Milestone 4.1 - Second Sprint: Task Implementations

Team Nexus (Group 20) · What's in My Food?

Members: Suyeon Park, Frank Liu, Eyad Ahmed, Alex An

Submitted: October 23, 2026


Location:
https://github.com/suyeon240park/ECE444-Group20/blob/main/docs/M4-sprint-2-report.pdf

---

1. Work backlog

Tool: GitHub Projects (https://github.com/users/suyeon240park/projects/2)

Sorted user stories:

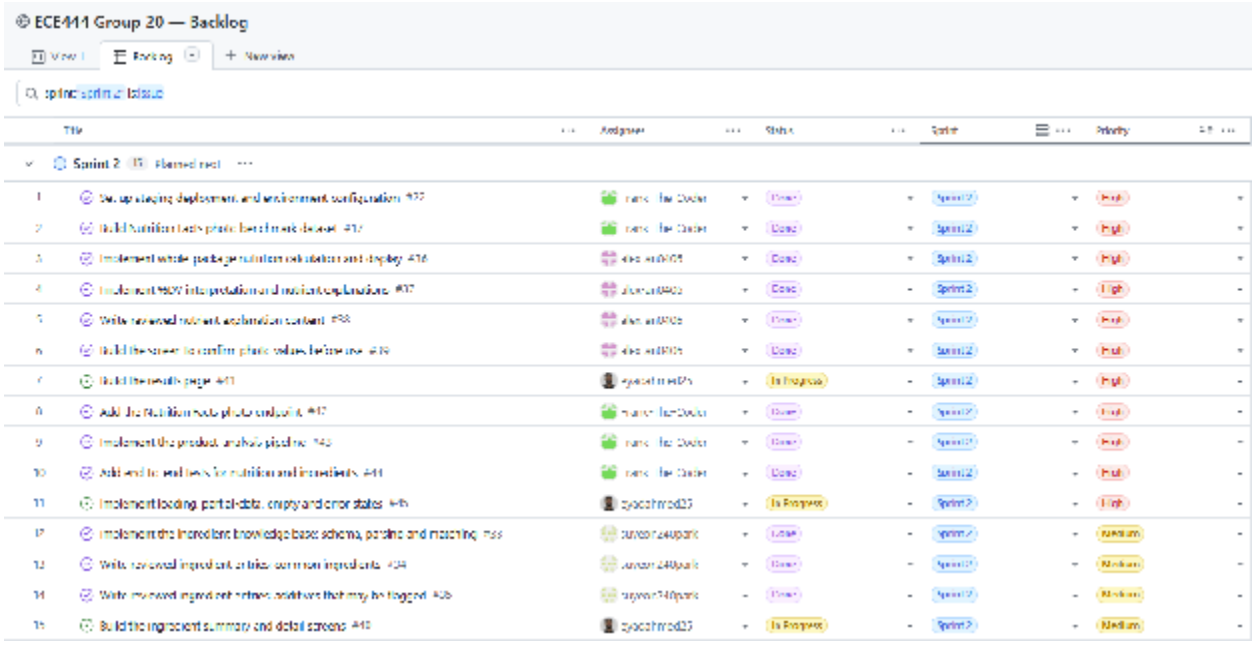

---

2. Sprint 2 summary and Sprint 3 plan

2.1 Sprint 2 summary

Goal: whole-package nutrition, nutrient explanations, ingredient analysis, and one results page.

Issue	Task	Story	Est. hours	Owner	Reviewer	Status
#33	Ingredient knowledge base: schema, parsing, matching	#9	12	Suyeon	Frank	Done (PR #47)
#34	Ingredient entries: common ingredients (sugar, salt, oils, flours, starches, emulsifiers)	#9	6	Suyeon	Alex	Done (PR #48)
#35	Ingredient entries: additives that may be flagged (colours, preservatives, sweeteners)	#9	6	Suyeon	Alex	Done (PR #54)
#36	Whole-package nutrition calculation and display	#2	10	Alex	Suyeon	Done (PR #49)

Issue	Task	Story	Est. hours	Owner	Reviewer	Status
#37	%DV interpretation and nutrient explanations	#3	10	Alex	Suyeon	Done (PR #53)
#38	Reviewed nutrient explanation content	#3	8	Alex	Frank	Done (PR #50)
#39	Screen to confirm photo values before use	#4, #10	6	Alex	Eyad	Done (PR #56)
#40	Ingredient summary and detail screens	#9	8	Eyad	Suyeon	Done (PR #61)
#41	Results page	#2, #3, #9	12	Eyad	Alex	Done (PR #60)
#42	Photo endpoint using the #16 prototype	#10, #4	6	Frank	Eyad	Done (PR #51)
#43	Pipeline that combines all analyses	#10, #2, #3, #9	12	Frank	Suyeon	Done (PR #52)
#17	50-photo label benchmark	#4	6	Frank	Eyad	Done (PR #57); second-teammate check of

Issue	Task	Story	Est. hours	Owner	Reviewer	Status
						photos 011–054 not done
#44	End-to-end tests for nutrition and ingredients	#2, #3, #9	6	Frank	Eyad	Done (PR #55)
#45	Loading, partial-data , empty and error states	#10, #2, #3, #9	6	Eyad	Alex	Done (PR #62)
#22	Staging deployment (carried over from sprint 1; moved from Eyad to Frank)	—	3	Frank	Suyeon	Done (PR #59)

Staging: https://whats-in-my-food.onrender.com

2.2 Sprint 3 plan

Goal: performance, usability, the photo path in the app, bug fixes and final deployment.

Issue	Task	Story	Est. hours	Depends on	Owner	Reviewer	PR by
#63	Connect the label-photo path: photo, confirm, results (record a demo video)	#10, #4	8	#39, #41	Frank	Alex	Nov 1
#70	Q3 readability check of explanation text	#11	4		Alex	Eyad	Nov 3
#18	Automated Q1 accuracy check of the benchmark	#4	6	#17	Eyad	Frank	Nov 6
#68	Q2 load test on staging (20 concurrent requests)	#5	8	—	Alex	Suyeon	Nov 8
#69	Q3 usability test with 5 participants, SUS (Alex is	#11	10	#63	Eyad	Suyeon	Nov 15

Issue	Task	Story	Est. hours	Depends on	Owner	Reviewer	PR by
	the second scorer)						
#71	Fix defects from Q1/Q2/Q3 and e2e results	#10, #2, #3, #9	8	All above	Suyeon	Alex	Nov 17
#73	UI polish from Q3 findings	#11	3		Suyeon	Frank	Nov 6
#72	Final deployment + Smoke test	—	6	all	Frank	Eyad	Nov 18

3. Individual task tables

Estimated hours were recorded at sprint 2 planning, before starting; actual hours are the time spent.

3.1 Liu's tasks

Liu's tasks for the 2nd sprint include:

Task	Estimated Time (hour)	Actual Time (hour)
#42 Photo endpoint using the #16 prototype	6	3
#43 Pipeline that combines all analyses	12	5
#17 50-photo label benchmark	6	4

Task	Estimated Time (hour)	Actual Time (hour)
#44 End-to-end tests for nutrition and ingredients	6	3
#22 Staging deployment (taken over from Eyad)	3	3
Review team-member pull requests timely and thoroughly	3	3
Participate actively in common team duties	2	4

Liu's tasks for the 3rd sprint include:

Task	Estimated Time (hour)	Actual Time (hour)
#63 Connect the label-photo path (record a demo video)	8	
#72 Final deployment and smoke test	6	
Review team-member pull requests timely and thoroughly	3	
Participate actively in common team duties	2	

3.2 Park's tasks

Park's tasks for the 2nd sprint include:

Task	Estimated Time (hour)	Actual Time (hour)
#33 Ingredient knowledge base: schema, parsing, matching	12	10
#34 Ingredient entries: common ingredients	6	4

Task	Estimated Time (hour)	Actual Time (hour)
#35 Ingredient entries: additives that may be flagged	6	4
Review team-member pull requests timely and thoroughly	3	4
Participate actively in common team duties	2	3

Park's tasks for the 3rd sprint include:

Task	Estimated Time (hour)	Actual Time (hour)
#71 Fix defects from Q1/Q2/Q3 and e2e results	8	
#73 UI polish from Q3 findings	3	
Review team-member pull requests timely and thoroughly	3	
Participate actively in common team duties	2	

3.3 Ahmed's tasks

Ahmed's tasks for the 2nd sprint include:

Task	Estimated Time (hour)	Actual Time (hour)
#40 Ingredient summary and detail screens	8	4
#41 Results page	12	4
#45 Loading, partial-data, empty and error states	6	4

Task	Estimated Time (hour)	Actual Time (hour)
#22 Finish staging deployment (moved to Frank on October 21)	3	0
Review team-member pull requests timely and thoroughly	3	3
Participate actively in common team duties	2	2

Ahmed's tasks for the 3rd sprint include:

Task	Estimated Time (hour)	Actual Time (hour)
#18 Automated Q1 accuracy check of the benchmark	6	
#69 Q3 usability test with 5 participants, SUS	10	
Review team-member pull requests timely and thoroughly	3	
Participate actively in common team duties	2	

3.4 An's tasks

An's tasks for the 2nd sprint include:

Task	Estimated Time (hour)	Actual Time (hour)
#36 Whole-package nutrition calculation and display	10	10
#37 %DV interpretation and nutrient explanations	10	9
#38 Reviewed nutrient explanation content	8	8

Task	Estimated Time (hour)	Actual Time (hour)
#39 Screen to confirm photo values before use	6	5
Check the ground truth of the 50-photo benchmark (#17)	1	1
Review team-member pull requests timely and thoroughly	3	4
Participate actively in common team duties	2	3

An's tasks for the 3rd sprint include:

Task	Estimated Time (hour)	Actual Time (hour)
#70 Q3 readability check of the explanation text	4	
#68 Q2 load test on staging	8	
Score the Q3 usability answers (second scorer, #69)	2	
Review team-member pull requests timely and thoroughly	3	
Participate actively in common team duties	2	
